

WEEKLY CONSTRUCTION PROGRESS REPORT

WEEK ENDING: November 7th, 2014

PROJECT WORK PERFORMED:

Two office trailers set up on-site.

Spray painted tree stumps for better visual recognition.

Removal activities are temporarily on hold pending approval of Site Operations Plan by USEPA.

WORK PROJECTED NEXT WEEK:

Full mobilization to site.

Verify personnel training and fitness for duty.

Review and revise Job Safety Analyses as necessary prior to issuance of Work Permits.

Begin general site set-up activities (safety meetings, site security, equipment staging).

Begin subsurface clearance protocol (ground-penetrating radar, GPS survey, one-call).

ACTION ITEMS/SAFETY:

FIELD HOUR AND LPS METRIC SUMMARY	WEEK		PROJECT TO DATE	
	AECOM (HOURS)	SUBS (HOURS)	AECOM (HOURS)	SUBS (HOURS)
	3	24	116	165
Field hours per LPO (Goal 1:400)	0:27		1:281	
NLI ratio (Goal 1:7)	0:0		0:2	
LPOs w/Quest. Items (Goal 90%)	0		1(100%)	
Peer to peer LPOs (Goal 80%)	0		1(100%)	


Site: Memphis - VCC Site



Site Office Trailer - Facing East




Spray Painted Tree Stumps – Facing North

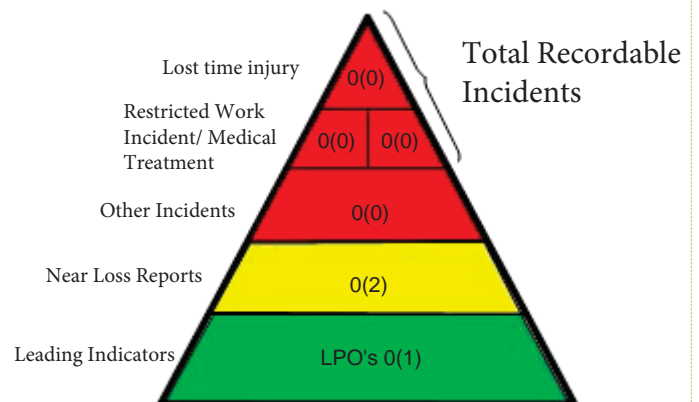

The first number represents the total for the week, the number in parentheses represents the total performed for the duration of the project

PROGRESS FIGURE

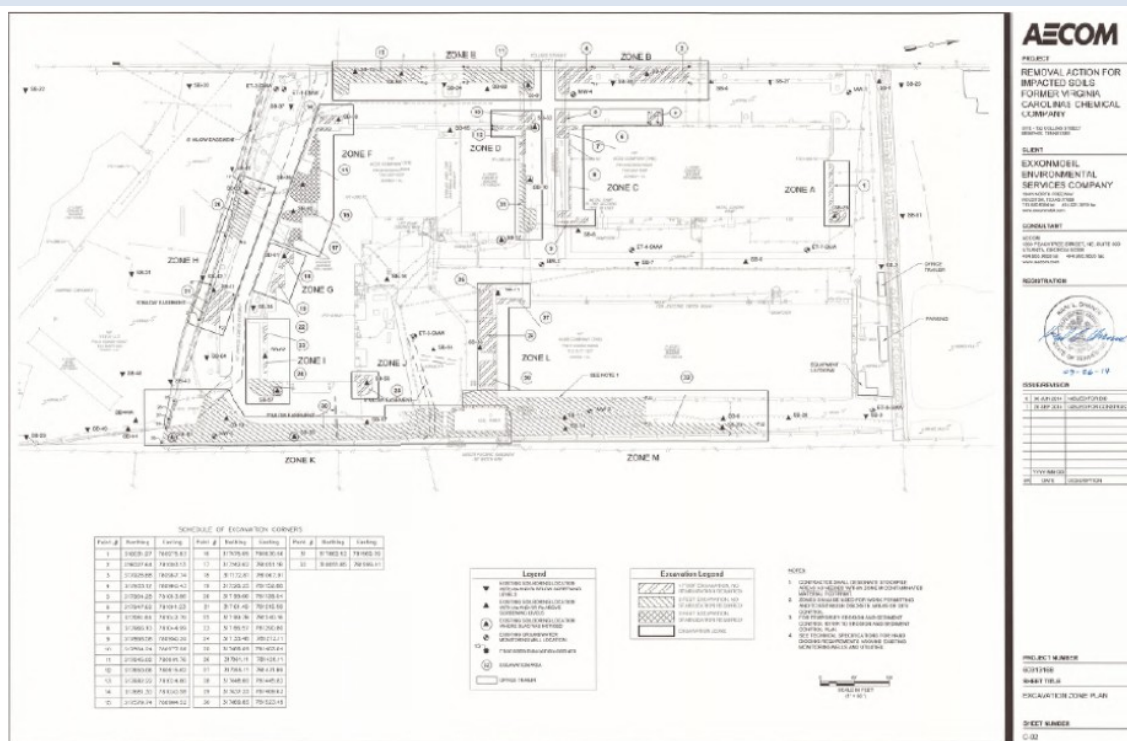

REMOVAL PROGRESS

	Cubic Yards (Initial Estimate)	Approximate Cubic Yards Excavated / Stabilized	Approximate Percent Complete
Excavation of Soil	N/A	N/A	N/A
Stabilization	N/A	N/A	N/A

AIR MONITORING

	Upwind	Down wind Excavation	Down wind
Data Ram 1000	N/A	N/A	N/A
Elf Air Sampling	N/A	N/A	N/A

PRECIPITATION:

TOTAL FOR THE WEEK: N/A PROJECT TOTAL: .59"

SITE VISITORS:

Name	Company	Date
