



614 Magnolia Avenue
Ocean Springs, MS 39564
Phone 228.818.9626
Fax 228.818.9631

January 17, 2011

Mr. Valmichael Leos
U.S. Environmental Protection Agency, Region 6
1445 Ross Avenue, Suite 1200
Dallas, Texas 75202-2733

Re: San Jacinto River Waste Pits Superfund Site
TCRA Weekly Progress Report No. 010 for January 10-14, 2011;
U.S. EPA Region 6, CERCLA Docket No. 06-12-10

Project Number: 090557-01

Dear Mr. Leos:

Attached please find TCRA Weekly Progress Report No. 010 for January 10-14, 2011. This report was prepared on behalf of the International Paper Company and McGinnes Industrial Maintenance Corporation for the San Jacinto River Waste Pits Superfund Site in Channelview, Texas. Should you have any questions, please contact me at (228) 818-9626 or email me at dkeith@anchorqea.com.

Sincerely,

John Laplante for David C. Keith
Project Coordinator

cc: Phil Slowiak, International Paper
Andrew Shafer, MIMC
Jennifer Sampson, Integral Corp.

Attachments

TCRA Weekly Progress Report No. 010
Submitted January 17, 2011
San Jacinto River Waste Pits Superfund Site
USEPA Region 6, CERCLA Docket No. 06-12-10
Channelview, Texas

This weekly progress report is submitted pursuant to the Administrative Settlement Agreement and Order on Consent for Removal Action: CERCLA Docket No. 06-12-10, Channelview, Texas, which became effective on May 11, 2010. The Respondents are International Paper Company (IP) and McGinnes Industrial Maintenance Corporation (MIMC).

A. Summary of Work Performed – Dates: January 10-14, 2011

The Respondents, Anchor QEA, and USA Environment, completed work on the following tasks:

- Submitted TCRA Weekly Progress Report No. 009 on January 10, 2011.
- Aggregate production has begun and is ongoing from Marble Falls quarry.
- USA Environment, MIMC, and Anchor QEA met on-site to review and plan locations for on-site stockpile and laydown areas.
- Began investigating on-site security options to be used during active TCRA construction, in light of the security issues discussed in TCRA Weekly Progress Report No. 009.
- USA Environment continued to develop contractor draft work plans described in the approved Removal Action Work Plan.
- Continued with best efforts to obtain access from TxDOT to construct a road to the waste pits, and with best efforts to obtain access from Big Star or an alternative location for use as a laydown/storage area.
- Installed USEPA site signs approved by Steve Tzhone and Donn Walters on January 13, 2011, at the approximate locations identified by Valmichael Leos during a site visit by Mr. Leos and Andrew Shafer of MIMC on January 7, 2011. Also, additional no trespassing signs were installed on the east bank Phase I fencing and on the existing free standing warning sign posts that were installed during the east bank Phase I fence installation.

B. Summary of Agency Communications

The written communications between the Respondents and USEPA, including and subsequent to the issuance of the Final Removal Action Work Plan, are summarized in the attached Table 1.

C. Summary of Sampling Results

- None for this report

TCRA Weekly Progress Report No. 010
Submitted January 17, 2011
San Jacinto River Waste Pits Superfund Site
USEPA Region 6, CERCLA Docket No. 06-12-10
Channelview, Texas

D. Problems, Delays, and Solutions

Access to construct a road on the TxDOT right of way and to build an equipment laydown and material storage area on the Big Star property or alternate property has not yet been obtained. The Respondents will continue to use their best efforts to obtain access.

On January 14, 2011, USEPA counsel transmitted to Respondents' counsel a Notice of Violation (NOV) via email. The NOV alleges violations of the AOC due to alleged failure of the Respondents to meet certain deadlines in the draft Schedule of Work. Respondents dispute the USEPA's allegations and will respond in accordance with the AOC.

To address security during construction, in light of the issues described in TCRA Weekly Progress Report No. 009, Respondents are investigating options including, but not limited to, remote cameras and/or third-party security for the Site.

E. Projected Work for the Next 2 Weeks – Dates: January 17-28, 2011

The Respondents, Anchor QEA, and USA Environment, expect to complete the following tasks in the next 2 weeks:

- Finalize lease for the alternate location for the laydown/storage area and prepare offsite stockpile areas to receive aggregate.
- Evaluate suitability of additional property as an additional alternative to Big Star site.
- Continue best efforts to obtain necessary access from TxDOT.
- Continue best efforts to obtain access from Big Star or an alternate location to use as a laydown/storage area.
- Continue to develop contractor work plans as referenced in Section 4.4 of the approved TCRA Removal Action Work Plan.
- Continue with production of aggregate, prepare and submit purchase orders for other materials and engage in other activities related to the TCRA work, provided that access from TxDOT and Big Star or an alternate property has been or is expected to be obtained.
- Commence site preparation work related to the laydown/storage area on the Big Star or alternate property and mobilize a trailer to be located on a portion of the laydown/storage area or alternate property, provided that access from Big Star or

TCRA Weekly Progress Report No. 010
Submitted January 17, 2011
San Jacinto River Waste Pits Superfund Site
USEPA Region 6, CERCLA Docket No. 06-12-10
Channelview, Texas

alternate property has been obtained.

- Take steps to address Site security.
- Schedule a pre-construction meeting, provided access has been obtained and office or office trailer has been mobilized for the project.

F. Schedule

The current project construction schedule is provided in the attached Figure 1. The schedule is dependent upon obtaining access from TxDOT to build a road and cross its right-of-way. After access is obtained, the schedule will be updated.

Prepared by:

John Laplante /for/

David C. Keith
Project Coordinator

Table of TCRA Communication
 Report No. 010 - January 17, 2011

Respondents Submittal Date	Respondents Communication Summary	Response from EPA Date	EPA Communication Summary	Notes
11/1/2010	Draft Final Removal Action Work Plan (RAWP) for Time Critical Removal Action	11/8/2010	TCRA Work Plan Approval with Modifications	
11/1/2010	Report on Respondents' best efforts to obtain access			
		11/2/2010	Letter from B. Nann regarding access	
11/9/2010	Memorandum - Review of Geomembrane Comments			
		11/9/2010	Email from B. Nann to Axe/Inglin requesting conference call on November 15, 2010 regarding TCRA access issues	
11/11/2010	Draft Pre-construction Meeting Agenda			
11/11/2010	Final Removal Action Work Plan (RAWP) for Time Critical Removal Action			
11/12/2010	Letter to EPA regarding access			
11/15/2010	Conference call with EPA B. Nann regarding access			Conference call to discuss the technical memorandum about water access versus land access to the TCRA Site. B. Nann stated that RAWP approval occurred 11/8/2010
11/15/2010	TCRA Weekly Progress Report 001 email from J. Laplante to V. Leos and five hard copies			
11/16/2010	Marine Access memo email from D. Keith to USEPA C. Sanchez			Email to USEPA technical team regarding issues related to water-only access to the TCRA site
		11/16/2010	Email from B. Nann to Respondents regarding meeting with Sam Coleman regarding access by water	
11/17/2010	Teleconference between D. Keith and C. Sanchez and V. Leos to discuss the 11/18 technical meeting at USEPA regarding site access			
		11/17/2010	Email from B. Nann to Respondents and TxDOT regarding meeting in Dallas on access issues	
11/17/2010	Email from IP counsel to B. Nann transmitting draft TxDOT license agreement			
11/17/2010	Emails from IP and MIMC counsel to B. Nann regarding meeting with Sam Coleman regarding access			Meeting with Sam Coleman, USEPA Superfund Division Director, to discuss access issues. Meeting took place 11/18/2010.
11/18/2010	Submittal of financial assurance by MIMC to cover revised TCRA cost estimate			
11/22/2010	TCRA Weekly Progress Report 002 email from J. Laplante to V. Leos and 5 hard copies			
11/22/2010	Financial assurance submission by IP with respect to the revised TCRA financial assurance amount			
11/23/2010	Submitted Notice of Start of Construction letter to USEPA			
11/23/2010	Prepared and submitted Request for State Historic Preservation Officer Consultation Form and supplemental information to Mark Wolfe, State Historic Preservation Officer			
11/29/2010	TCRA Weekly Progress Report 003 email from W. Mears to V. Leos and 5 hard copies			
11/30/2010	Submitted Request for Section 401 of the CWA Consultation Review to S. Reilly of TCEQ, with copy to V. Leos			
11/30/2010	Preliminary (unvalidated) Big Star property chemistry data submitted to V. Leos by D. Keith via email			
11/30/2010			Email from V. Leos of USEPA regarding status of preliminary data from Big Star soil sampling	
11/30/2010			Email from B. Nann of USEPA to Respondents' counsel regarding the status of the Big Star sampling results	
11/30/2010	Submitted proposed road license agreement with TxDOT, signed by Respondents' counsel, to B. Nann of USEPA			

Table of TCRA Communication
 Report No. 010 - January 17, 2011

Respondents Submittal Date	Respondents Communication Summary	Response from EPA Date	EPA Communication Summary	Notes
11/30/2010	Submitted letter to EPA describing Respondents' "best efforts" to obtain access from Big Star and TxDOT and requesting an extension of time to obtain access	12/3/2010		
12/1/2010	Email from MIMC's counsel on behalf of Respondents to B. Nann urging USEPA's quick turnaround on analysis of Big Star soil sample results			
12/1/2010	Email to V. Leos from Project Coordinator updating Big Star soil sampling data			
12/2/2010			Email from B. Nann to Respondents' counsel regarding status of USEPA's analysis of Big Star's sample results and scheduling of conference call to discuss access issues	
12/2/2010	Email from IP Counsel on behalf of Respondents' to B. Nann and S. Coleman regarding obstacles to obtaining access from Big Star and TxDOT	12/3/2010		
12/3/2010			Email from B. Nann to Respondents' counsel and S. Coleman responding to Respondents' December 2, 2010 email regarding obstacles to obtaining access	
12/3/2010	Email from IP counsel on behalf of Respondents' to B. Nann and S. Coleman responding to EPA's December 3, 2010 email regarding access issues			
12/3/2010			Letter from USEPA responding to Respondents' November 30, 2010 letter regarding best efforts, denying extension of time to obtain access	
12/6/2010	TCRA Weekly Progress Report 004 email from J. Laplante to V. Leos and five hard copies			
		12/6/2010	Email from B. Nann to Respondents' counsel regarding TxDOT and Big Star access issues and status of Big Star as PRP	
12/6/2010	Email from IP counsel to B. Nann of behalf of Respondents' regarding van der Horst Site access agreement	12/6/2010	Email from B. Nann to Respondents' counsel regarding van der Horst access agreement	
12/6/2010	Email from IP counsel to USEPA counsel handling van der Horst site regarding access agreement			
12/6/2010	Email from B. Nann to Respondents' counsel regarding scheduling of conference call on access issues			Conference call between Respondents' counsel and USEPA regarding TxDOT access takes place on December 7, 2010
12/6/2010	Email from IP counsel on behalf of Respondents' to B. Nann regarding proposed Big Star lease terms			
12/6/2010	Email from IP counsel on behalf of Respondents' to B. Nann regarding signed access agreement with Big Star for installation of Phase II fencing			
		12/7/2010	Email from B. Nann stating USEPA's approval of Big Star property as a laydown area	
12/7/2010	Email to B. Nann from MIMC counsel on behalf of Respondents' regarding scheduling of conference call with USEPA and Big Star regarding lease			
		12/7/2010	Email from B. Nann to Respondents' counsel regarding her call to Big Star attorney	
		12/7/2010	Email from B. Nann regarding status of proposed TxDOT access agreement language	
12/7/2010	Emails to B. Nann from IP counsel on behalf of Respondents' regarding proposed TxDOT license agreement			
12/7/2010	Email from IP counsel on behalf of Respondents' to B. Nann regarding status of her conversation with Big Star counsel			
		12/8/2010	Email from B. Nann to Respondents' counsel regarding TxDOT and Big Star access status	
12/8/2010	Email to B. Nann from IP counsel on behalf of Respondents' regarding TxDOT and Big Star access issues			
12/8/2010	Email to Big Star counsel and B. Nann from IP counsel on behalf of Respondents' regarding status of lease			
		12/8/2010	Email from USEPA counsel for van der Horst site regarding site access agreement with TxDOT	

Table of TCRA Communication
 Report No. 010 - January 17, 2011

Respondents Submittal Date	Respondents Communication Summary	Response from EPA Date	EPA Communication Summary	Notes
12/8/2010	Email from IP counsel to USEPA counsel for van der Horst site regarding access agreement with TxDOT			
12/9/2010	Email from A. Shafer (MIMC) to V. Leos and S. Tzhone requesting guidance regarding sign size			
12/9/2010			Email from USEPA V. Leos with a copy of USEPA Pollution Report (POLREP) for the TCRA	
12/10/2010	Email to B. Nann from MIMC counsel on behalf of Respondents' regarding status of TxDOT and Big Star access issues			
12/10/2010	Email to B. Nann from IP counsel on behalf of Respondents' asking if B. Nann would schedule a conference call between Big Star, USEPA, and Respondents' counsel			
12/10/2010	Email to B. Nann from MIMC counsel on behalf of Respondents regarding Big Star Status as a PRP			
12/13/2010	TCRA Weekly Progress Report 005 email from J. Laplante to V. Leos and five hard copies			
12/13/2010	Email to B. Nann from IP counsel on behalf of Respondents regarding status of Big Star and TxDOT access issues			
12/15/2010	Email to B. Nann from MIMC counsel on behalf of Respondents regarding Big Star's position on lease	12/16/2010	Email from B. Nann regarding Big Star's demand for a release of all claims	
12/17/2010	Email to B. Nann from IP counsel on behalf of Respondents regarding Big Star's position on access and requesting EPA's assistance			
12/17/2010	Email to B. Nann from IP counsel on behalf of Respondents asking for conference call to discuss Big Star's demand for a release as a condition of access			
12/20/2010	TCRA Weekly Progress Report 006 email from J. Laplante to V. Leos and five hard copies			
12/21/2010	Email to B. Nann from IP counsel on behalf of Respondents regarding latest demand for full release from Big Star counsel and requesting opportunity to discuss same			
		12/23/2010	Letter from USEPA V. Leos to Respondents in regarding TxDOT access	
12/27/2010	TCRA Weekly Progress Report 007 email from J. Laplante to V. Leos and five hard copies			
		12/27/2010	Email to Respondents' counsel from B. Nann of USEPA forwarding copy of EPA's 12/23/2010 correspondence (letter was not received by Respondents until it was forwarded by USEPA's counsel on December 27 and original sent by mail was not received until December 30, 2010)	
		12/30/2010	Letter from USEPA V. Leos to Respondents in regarding TxDOT access, as followup to USEPA letter dated 12/23/2010	
12/30/2010	Letter to V. Leos of USEPA from MIMC counsel on behalf of Respondents in response to USEPA's letters dated 12/23/2010 and 12/30/2010 and initial force majeure notice			


Table of TCRA Communication
 Report No. 010 - January 17, 2011

Respondents Submittal Date	Respondents Communication Summary	Response from EPA Date	EPA Communication Summary	Notes
1/3/2011	TCRA Weekly Progress Report 008 email from J. Laplante to V. Leos and five hard copies			
1/4/2011	Email to USEPA from D. Shafer of MIMC regarding delivery of TCRA financial assurance instruments to EPA on 11/19/2010			
1/4/2011	Letter to V. Leos of USEPA from MIMC counsel regarding force majeure event			
1/4/2011	Letter to V. Leos of USEPA from IP counsel joining in MIMC's letter dated 1/4/2011 regarding force majeure event			
1/4/2011	Memorandum to V. Leos of USEPA on the Evaluation of the Potential Change in Water Surface Elevation Due to the Placement of the Capping Remedy			
		1/4/2011	Letter to MIMC from V. Leos of USEPA regarding financial assurance	
1/5/2011	Letter to EPA from IP counsel on behalf of Respondents regarding access issues and notice of force majeure			
		Undated	Letter to Respondents' Project Coordinator from V. Leos regarding USEPA's site inspection of December 8, 2010 and upcoming scheduled work activities. The letter was received on 1/6/2011.	
		1/6/2011	Email to D. Shafer of MIMC from B. Werner of USEPA regarding need for duplicates of TCRA financial assurance instruments	
1/6/2011	Email from D. Shafer of MIMC on behalf of Respondents regarding Site signs and buoys and intent to inspect fencing and signs on 1/7/2011			
		1/7/2011	Email from V. Leos of USEPA stating that representatives from Harris County and TCEQ and himself would be visiting the Site on 1/7/2011	
1/10/2011	TCRA Weekly Progress Report 009 email from J. Laplante to V. Leos and five hard copies			
1/12/2011	Email to B. Nann of USEPA from MIMC's counsel on behalf of Respondents regarding TxDOT and Big Star access issues and Big Star's prospective status as a PRP	1/13/2011	Email from B. Nann of USEPA to Respondents' counsel (in response to 1/12/2011 email from MIMC's counsel) regarding TxDOT negotiations, alternative laydown area, and Big Star's status as PRP	
1/13/2011	Email from IP's counsel to B. Nann of USEPA responding to her 1/13/2011 email regarding TxDOT access negotiations	1/14/2011	Email from B. Nann of USEPA to Respondents' counsel responding to 1/13/2011 email from IP's counsel regarding TxDOT access negotiations	

Table of TCRA Communication
 Report No. 010 - January 17, 2011

Respondents Submittal Date	Respondents Communication Summary	Response from EPA Date	EPA Communication Summary	Notes
		1/13/2011	Email from B. Nann of USEPA to Respondents' counsel (responding to 1/12/2011 email from MIMC's counsel) addressing "ability to pay" issue for Big Star	
		1/14/2011	Email from B. Nann of USEPA to Respondents' counsel transmitting USEPA letter regarding Notice of Violation	

**-DRAFT FINAL SCHEDULE-
SAN JACINTO RIVER WASTE PITS SUPERFUND SITE**

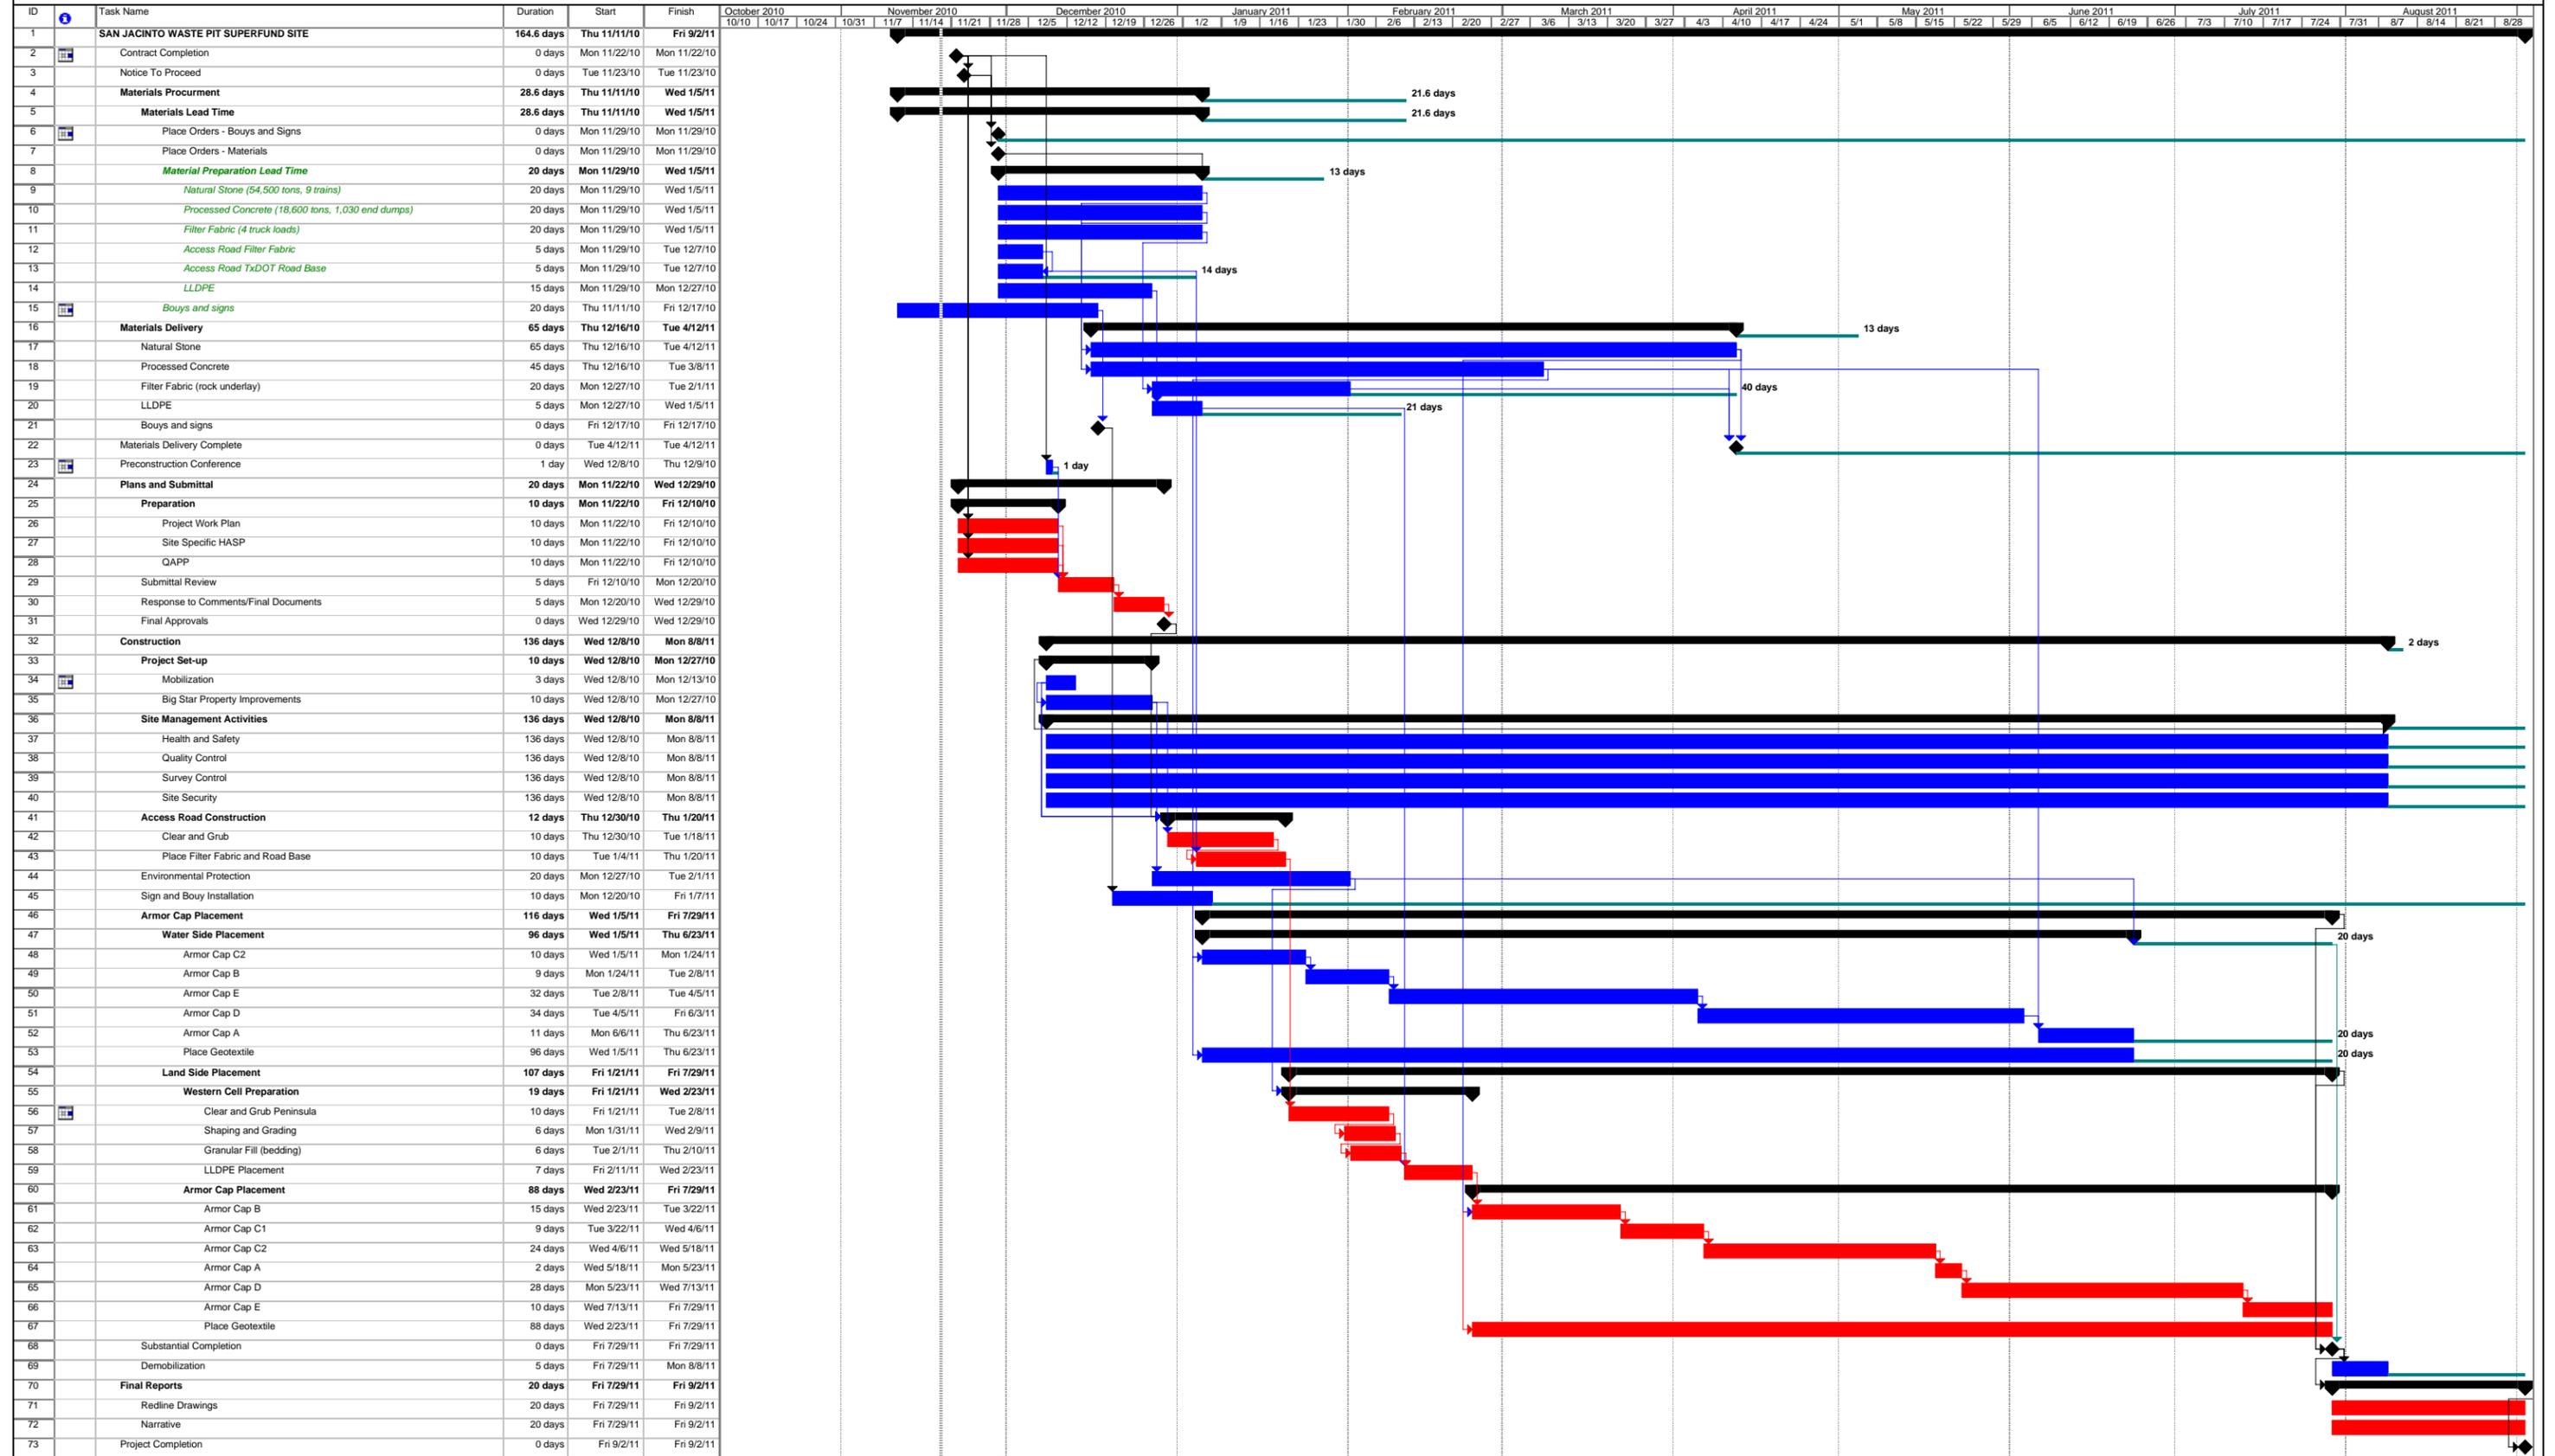

Project: San Jacinto River Waste Pits Superfund Site
 Draft Schedule
 Date: Fri 11/19/10

█ Critical Task
█ Progress
█ Milestone
█ Slack
◆ Slippage
█ Summary
█ Project Summary
█ Rolled Up Critical
█ Rolled Up Critical Split
█ External Tasks
█ External Milestone
█ Deadline
↓

Page 1
