

## WEEKLY CONSTRUCTION PROGRESS REPORT

WEEK ENDING: 11-14-2014

### PROJECT WORK PERFORMED:

- Project kick-off meeting was completed. Those in attendance included AECOM, Envirocon, GPRS, SWS and Allen & Hoshall
- Health and safety oversight and stewardship
- Allen & Hoshall began demarcating proposed Excavation Zones
- Soft Excavation Utility Clearance Survey (Geophysics) began and was completed
- Review of equipment (XRF, DataRAM, Air Sampling pump, weather station)
- Personal air Sampling - Negative Exposure Assessment began
- Baseline air monitoring began and was completed
- Exclusion zone set-up proceeded and continued
- Brush clearing began and was completed at Zone M.

### WORK PROJECTED NEXT WEEK:

- Health and safety oversight and stewardship
- Allen & Hoshall will continue to demarcate proposed Excavation Zones and as-built surveying.
- Personal air Sampling will continue as required
- Perimeter air monitoring will continue
- Exclusion zone set-up will continue as required
- Soft digging to expose utilities and other anomalies identified during the geophysics survey will proceed beginning at Zone M
- Brush clearing will continue as required.

### ACTION ITEMS/SAFETY:

- Power needs to be connected to the temporary office spaces.

FIELD HOUR AND LPS METRIC SUMMARY	WEEK		PROJECT TO DATE	
	AECOM (HOURS)	SUBS (HOURS)	AECOM (HOURS)	SUBS (HOURS)
	150	539	266	704
Field hours per LPO (Goal 1:200)	1:172		1:194	
NLI ratio (Goal 1:7)	0:0		0:2	
LPOs w/Quest. Items (Goal 90%)	2/4 (50%)		3/5 (60%)	
Peer to peer LPOs (Goal 80%)	3/4 (75%)		4/5 (80%)	


Site: Memphis - VCC Site



Soft Excavation Utility Clearance Survey




Brush Clearing at Zone M

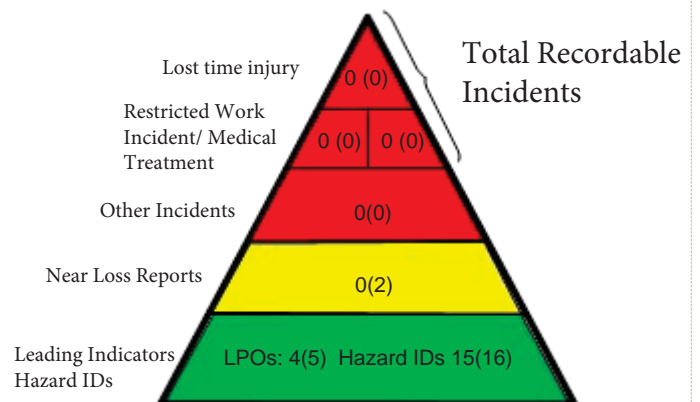

The first number represents the total for the week, the number in parentheses represents the total performed for the duration of the project

## PROGRESS FIGURE

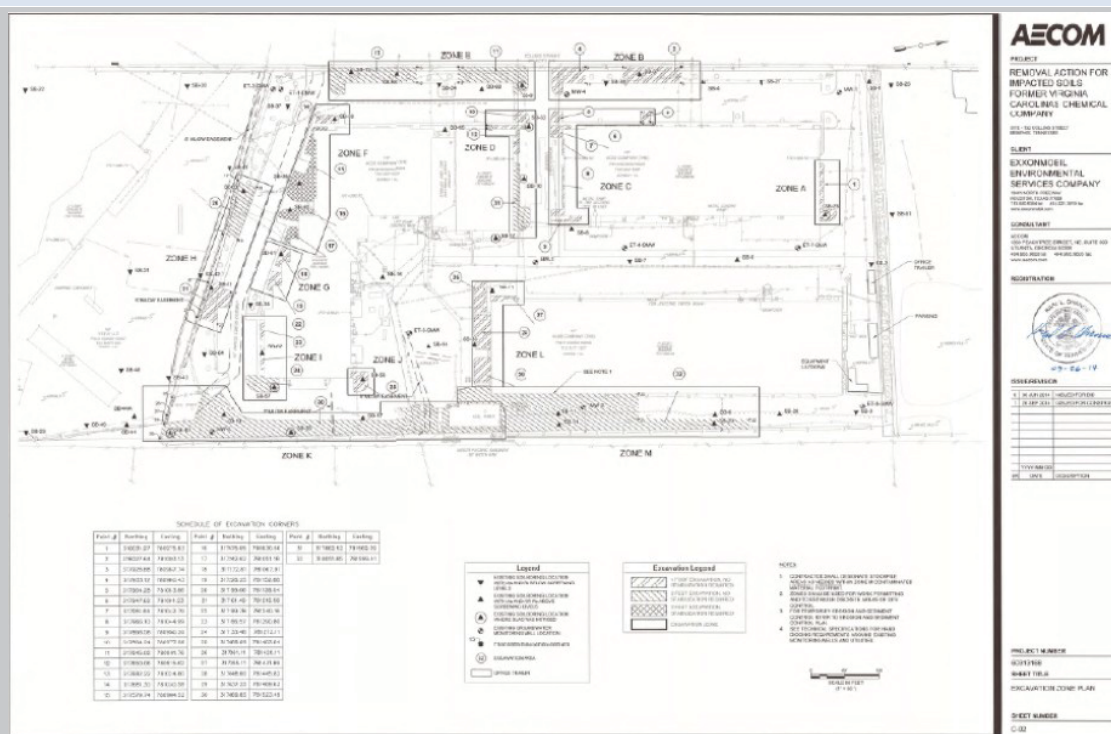

## REMOVAL PROGRESS

	Cubic Yards (Initial Estimate)	Approximate Cubic Yards Excavated / Stabilized	Approximate Percent Complete
Excavation of Soil	8,657 Tons	0	0%
Stabilization	575 Tons	0	0%

## AIR MONITORING

	Upwind	Downwind Excavation	Downwind along Collins Street
Data Ram 1000AN	X	X	X
Aircheck 224-52 Air Sampling	X	X	X

PRECIPITATION:

TOTAL FOR THE WEEK: 0.3"      PROJECT TOTAL: 0.89"

## SITE VISITORS:

Name	Company	Date
Jewel Cox	ExxonMobil	11-10 to 11-12
Cris Altman	AECOM	11-10 to 11-13
Kris Brobst	AECOM	11-11 to 11-12
Joel Larkin	ExxonMobil	11-12
